September 2026 Quarterly Activities Report

For personal use only

Highlights:

Youanmi Gold Mine

- **Youanmi fully permitted following the granting of final works approval early in the quarter**
- **Processing plant construction progressing to plan and 39% complete at quarter end.**
- **A total of 1,665m of lateral underground development completed**
- **Ore mined totalled 20 kt at 2.75 g/t Au for 1.8 koz, while the surface stockpile reached 48 kt at 3.05g/t Au for 4.7 koz, both ahead of the DFS schedule**
- **Underground diamond drilling returned significant results at United North, with the infill drilling program remaining on schedule**
- **Surface growth program commenced down dip of United North**
- **Power supply contract executed, with the oxygen supply contract the only remaining major contract and close to execution**
- **Updated Youanmi Mineral Resources and Ore Reserves, with growth of 4% to 2,195 koz and 8% to 727 koz respectively**

Corporate

- **Financial Close achieved after quarter end, with first drawdown completed on 2 October 2026**
- **Cash balance of $59.3 million at 30 September 2026, followed by a $90.2 million drawdown after quarter end**
- **Native title agreement executed with Badimia Barna Native Title Claim Applicant, covering the Youanmi Gold Mine project area**

West Australian gold development company Rox Resources Limited **("Rox" or "the Company") (ASX: RXL)** is pleased to present its quarterly report for the period ended 30 September 2026.

Managing Director & CEO Mr Phillip Wilding commented:

"Works have continued to accelerate at the Youanmi Gold Mine over the last quarter, with mining activity increasing, processing plant advancing, underground drilling underway and high-grade surface ore stockpiles building.

"EPC contractor Interquip has made strong progress with processing plant construction, with the several key long-lead items either now in country or en route. Coupled with tailings storage facility construction tracking ahead of schedule, this keeps Rox firmly on track to achieve first gold in mid-CY2027.

"Mining has continued to ramp up following the introduction of a second development team focused on advancing Youanmi Main. Underground development rates continue to exceed DFS expectations, while surface stockpiles are larger and higher grade than forecast. Infrastructure is also in place to support production stoping commencing in the December quarter. Underground diamond drilling is delivering

encouraging results, with several areas exceeding expectations from the recent Mineral Resource update, further de-risking the start-up of Youanmi.

"Growth drilling has commenced in the deeper sections of United North, targeting resource conversion and potential resource growth down dip of the orebody. This work is intended to support Rox's aspiration to deliver an expanded mine plan and mine life, targeting production of 150,000oz per annum.

"It has been a transformational quarter at the Youanmi Gold Mine, with further activity planned over the coming quarter as we continue to execute our pathway to production and move closer to establishing Rox as one of Western Australia's next gold producers."

Mining Operations

During the September quarter, Rox achieved total underground lateral development advance of 1,665m, bringing total advance to 3,795m across the Youanmi Gold Mine (see Figure 1 and Figure 2). This represents a 49% increase in lateral development compared with the June quarter, supported by the mobilisation of a second development jumbo in June

Ore drive development commenced on the United North 2356, 2341 and 2325 levels, with a total of 20,584t @ 2.75 g/t Au, containing 1,818 oz of gold, delivered to the run-of-mine (ROM) stockpile. Total ROM stocks at quarter end stood at 47,955t @ 3.05 g/t Au, containing 4,700 oz of gold and ahead of schedule in comparison to the Definitive Feasibility Study (DFS).

Establishment of the return airway system continued, with the exhaust raise completed to the 2280 level. Temporary primary ventilation fans were also installed underground, providing additional airflow and enabling development to advance across additional mining levels.

Importantly, the first United North escapeway to surface was installed ahead of planned stoping commencement in the December quarter.

Development at Youanmi Main focused on rehabilitating the existing decline and advancing capital infrastructure headings for primary ventilation, escapeways, dewatering and power. Establishment of initial level access points for ore development also commenced.

Underground diamond drilling continued at United North, with 9,622m of grade control drilling completed during the quarter.

For personal use only

For personal use only

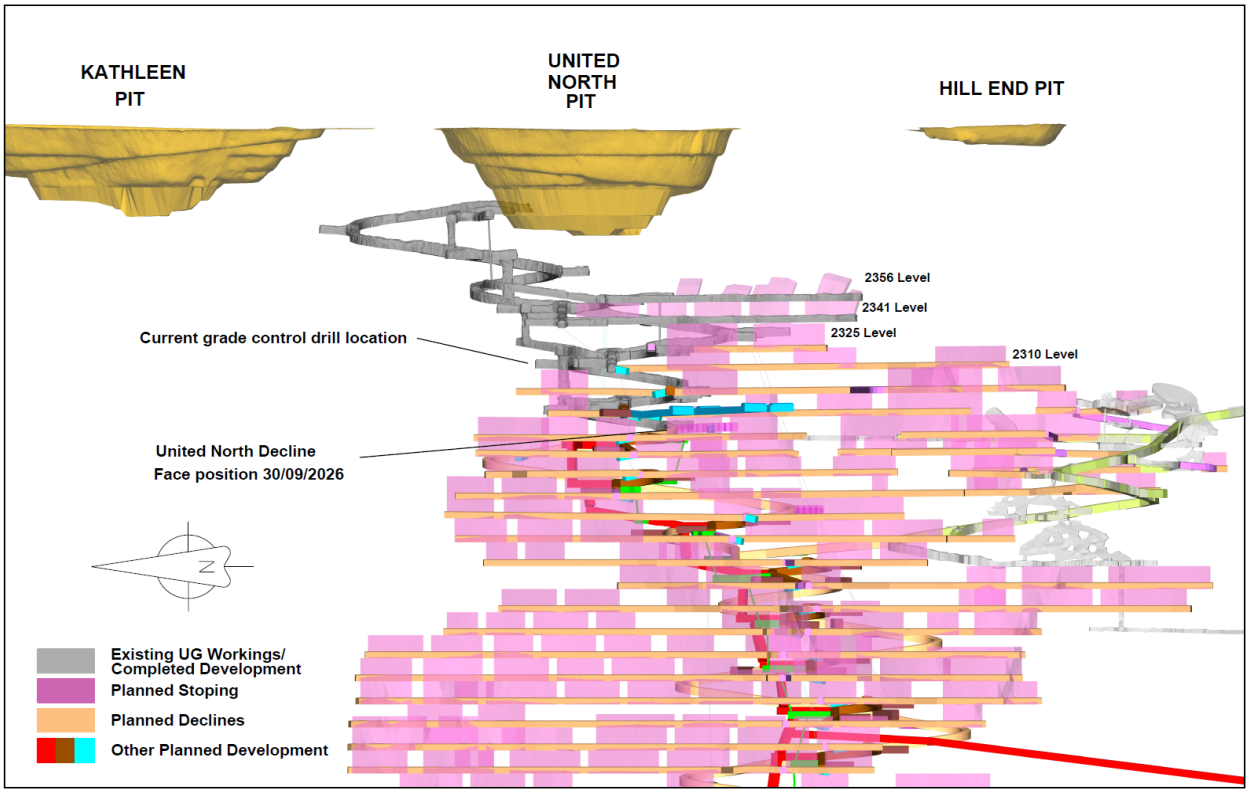


Figure 1 – Development progress at United North

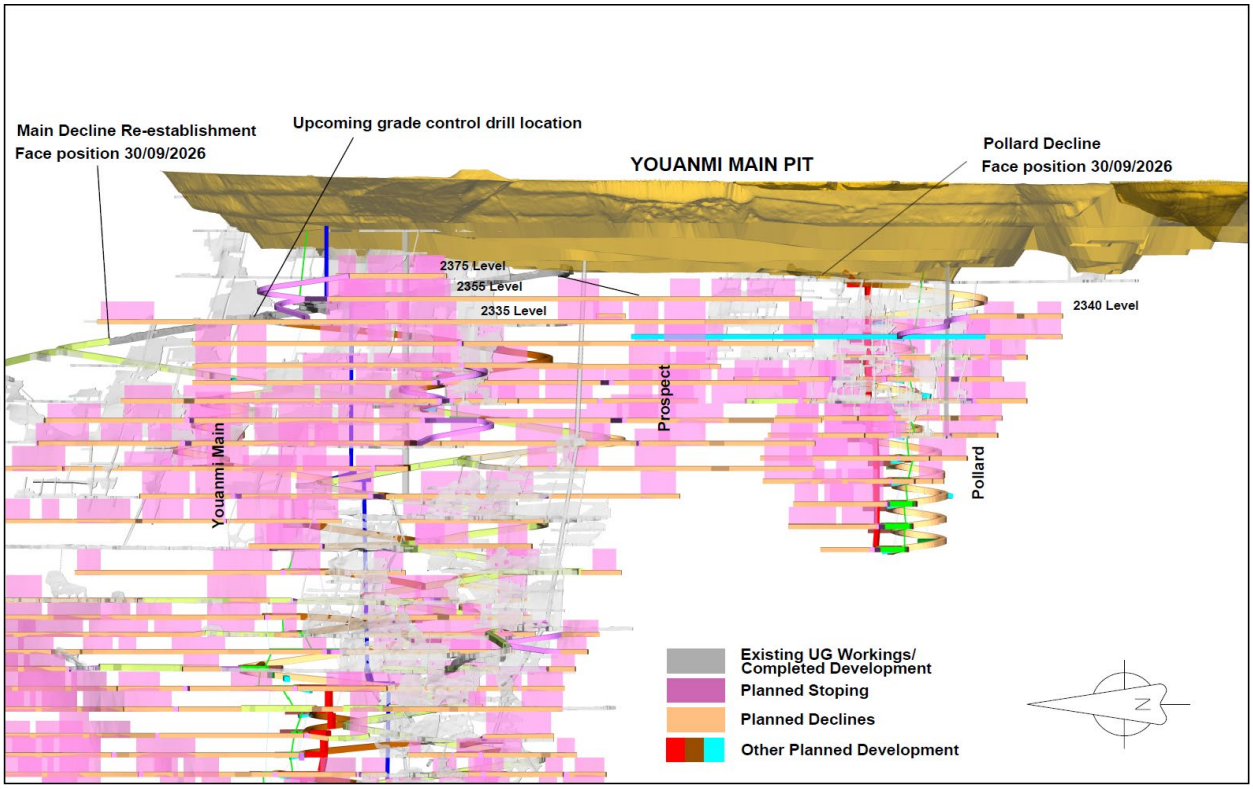


Figure 2 – Development progress at Youanmi and Pollard Declines (as built)

For personal use only

Processing Plant Construction

Interquip and Glencore Technology continued to advance detailed design of the Youanmi Processing Plant (Figure 3), with construction drawings issued to support on-site works.



Figure 3 – Youanmi Processing Plant working layout

Fabrication of the ball mill and crushers is complete, with equipment either in Perth or en-route. Albion leach tank platework is nearing completion, with two shipments having departed port and trial assemblies of the remaining tanks underway (Figure 4). The IsaMill is also nearing completion and is scheduled for delivery to Perth during the December Quarter.

Overall, equipment delivery and construction remains on schedule, supporting Rox's target of first gold in mid-CY2027.



Figure 4 – Albion Leach tank trial assembly at fabrication workshop

For personal use only

Contract negotiations for the final remaining major contract, the oxygen supply agreement, are nearing completion.

Site civil works continued in line with schedule during the quarter (Figure 5), with key construction milestones achieved, including:

- Completion of all ring beam footings for the CIL tanks.
- Platework and strake welding completed on six CIL tanks, with the remaining two tanks well advanced,
- Concrete pours completed for the crusher footings, screen house, conveyor footings, fine ore bin, ball mill raft slab, IsaMill raft slab and thickener tank footings,
- Construction of ring beam footings for the Albion leach tanks,
- Warehouse concrete slab poured, with shed construction commenced,
- In-ground services installation commenced for the power station.



Figure 5 – Youanmi Processing Plant construction

Tailings Storage Facility

Construction of the new tailings storage facility (TSF3) commenced during the quarter, with vegetation clearing and topsoil stripping & stockpiling completed. Bulk earthworks are progressing on the starter dam embankment, diversion drain and cut-off trench (Figure 6), alongside clearing of the tailings pipeline corridor.



Figure 6 – Youanmi Tailings Storage Facility earth works

For personal use only

Project Permitting

Rox obtained the final major approval in July, with the granting of the Works Approval, completing the permitting requirements for construction and operation of the Youanmi Gold Mine.

Updated Mineral Resource and Ore Reserve Estimate

The Company released an updated Mineral Resource and Ore Reserve estimate during the quarter (see ASX announcement "Annual Update to Mineral Resources and Ore Reserve at Youanmi Gold Mine" on 9 September 2026), following completion of the surface drilling campaign at United North earlier in the year[1].

The update excludes results from the Interceptor surface drilling program and the recently commenced underground grade control drilling program, as these were received after the estimation cut-off date.

The most significant change to the updated Mineral Resource Estimate was an increase in surface Indicated Resources, with tonnes increasing by approximately 34% and contained gold ounces increasing by approximately by 31%.

The updated Ore Reserve is 4.8 Mt @ 4.7 g/t for 727koz of contained gold, representing an 8% increase on the 30 October 2025 Ore Reserve after accounting for depletion to 30 June 2026.

A summary of the 2026 Mineral Resources and Ore Reserves is **provided in Tables 1 and 2.**

Mine Geology

During the quarter, ore drive development continued ahead of the production rate scheduled in the DFS, with the 2356 and 2341mRL ore drives extending approximately 125m further along strike than originally designed in the DFS (Figure 7).

Previously reported[2] surface drilling supported the extension to these ore drives. This was further corroborated by underground infill drilling (Figure 8) and production face sampling (Figure 7).

Preparation works for production stoping on both levels are complete, stope planning has commenced and production drilling was scheduled to commence in mid-October 2026

Underground diamond drilling completed within the quarter infilled the southern end of United North down to the 2295mRL ore drive level, where development has since commenced (Figure 8).

Underground drilling to date has confirmed grade estimates in the 2025 Mineral Resource Estimate[3] which underpinned the DFS, while also identifying areas of potential upside. These include high-grade plunging shoots identified through core and face mapping.

Grade control modelling parameters were updated to reflect the new statistics generated for the United North Mineral Resource Estimate. Grade control estimation for mining has since been completed, supporting the next stage of stope planning.

[1] ASX RXL 21st April 2026, "Drilling identifies high-grade ounces outside of DFS mine plan"

[2] ASX RXL 21st April 2026, "Drilling identifies high-grade ounces outside of DFS mine plan"

[3] ASX RXL 21st July 2025, "Underground Resource Increased to 2.1 Moz"

personal use only

Table 1. Summary of Mineral Resources – 2026

Mineral Resource Estimate	Measured			Indicated			Inferred			Total		
	Mt	g/t Au	koz Au	Mt	g/t Au	koz Au	Mt	g/t Au	koz Au	Mt	g/t Au	koz Au
Surface	-	-	-	1.0	2.0	62	0.6	1.4	25	1.5	1.8	87
Underground	-	-	-	7.5	6.4	1,541	3.4	5.2	563	10.9	6.0	2,105
Stockpiles	-	-	-	0.0	3.1	3	-	-	-	0.0	3.1	3
Total	**-**	**-**	**-**	**8.5**	**5.9**	**1,606**	**3.9**	**4.7**	**588**	**12.4**	**5.5**	**2,195**

Explanatory Notes:

1. The Mineral Resource is classified in accordance with the Australasian Code for Reporting of Exploration Results, Mineral Resources and Ore Reserves (the JORC Code) 2012 edition;

2. Tonnes are reported as million tonnes (Mt) and rounded to the nearest 100,000; grade reported in grams per tonne (g/t) to the nearest tenth; gold (Au) ounces are reported as thousands rounded to the nearest 1,000;

3. The surface portion of the Mineral Resource is above the top of fresh rock, and above 0.5 g/t Au cut-off grade;

4. The Underground Resource is the portion of the Mineral Resource below the top of fresh rock, and above a 2.5 g/t Au cut-off grade; and

5. Due to rounding, some numbers in this table may not add up.

Table 2. Summary of Ore Reserves - 2026

Ore Reserve Estimate	Proved			Probable			Total		
	Mt	g/t Au	koz Au	Mt	g/t Au	koz Au	Mt	g/t Au	koz Au
Youanmi	0	0.0	0	4.7	4.8	724	4.7	4.8	724
ROM & Stockpiles	0	0.0	0	0.0	3.1	3	0.0	3.1	3
Total	**0**	**0.0**	**0**	**4.8**	**4.7**	**727**	**4.8**	**4.7**	**727**

Explanatory Notes:

1. The reported Mineral Resources are inclusive of the Ore Reserves and surface stockpiles;

2. Tonnes are reported as million tonnes (Mt) and rounded to the nearest 100,000; grade reported in grams per tonne (g/t) to the nearest tenth; gold (Au) ounces are reported as thousands rounded to the nearest 1,000;

3. The Ore Reserve has been estimated using cut-off grades calculated on a gold price of A$3,200/oz; and

4. Due to rounding, some numbers in this table may not add up.

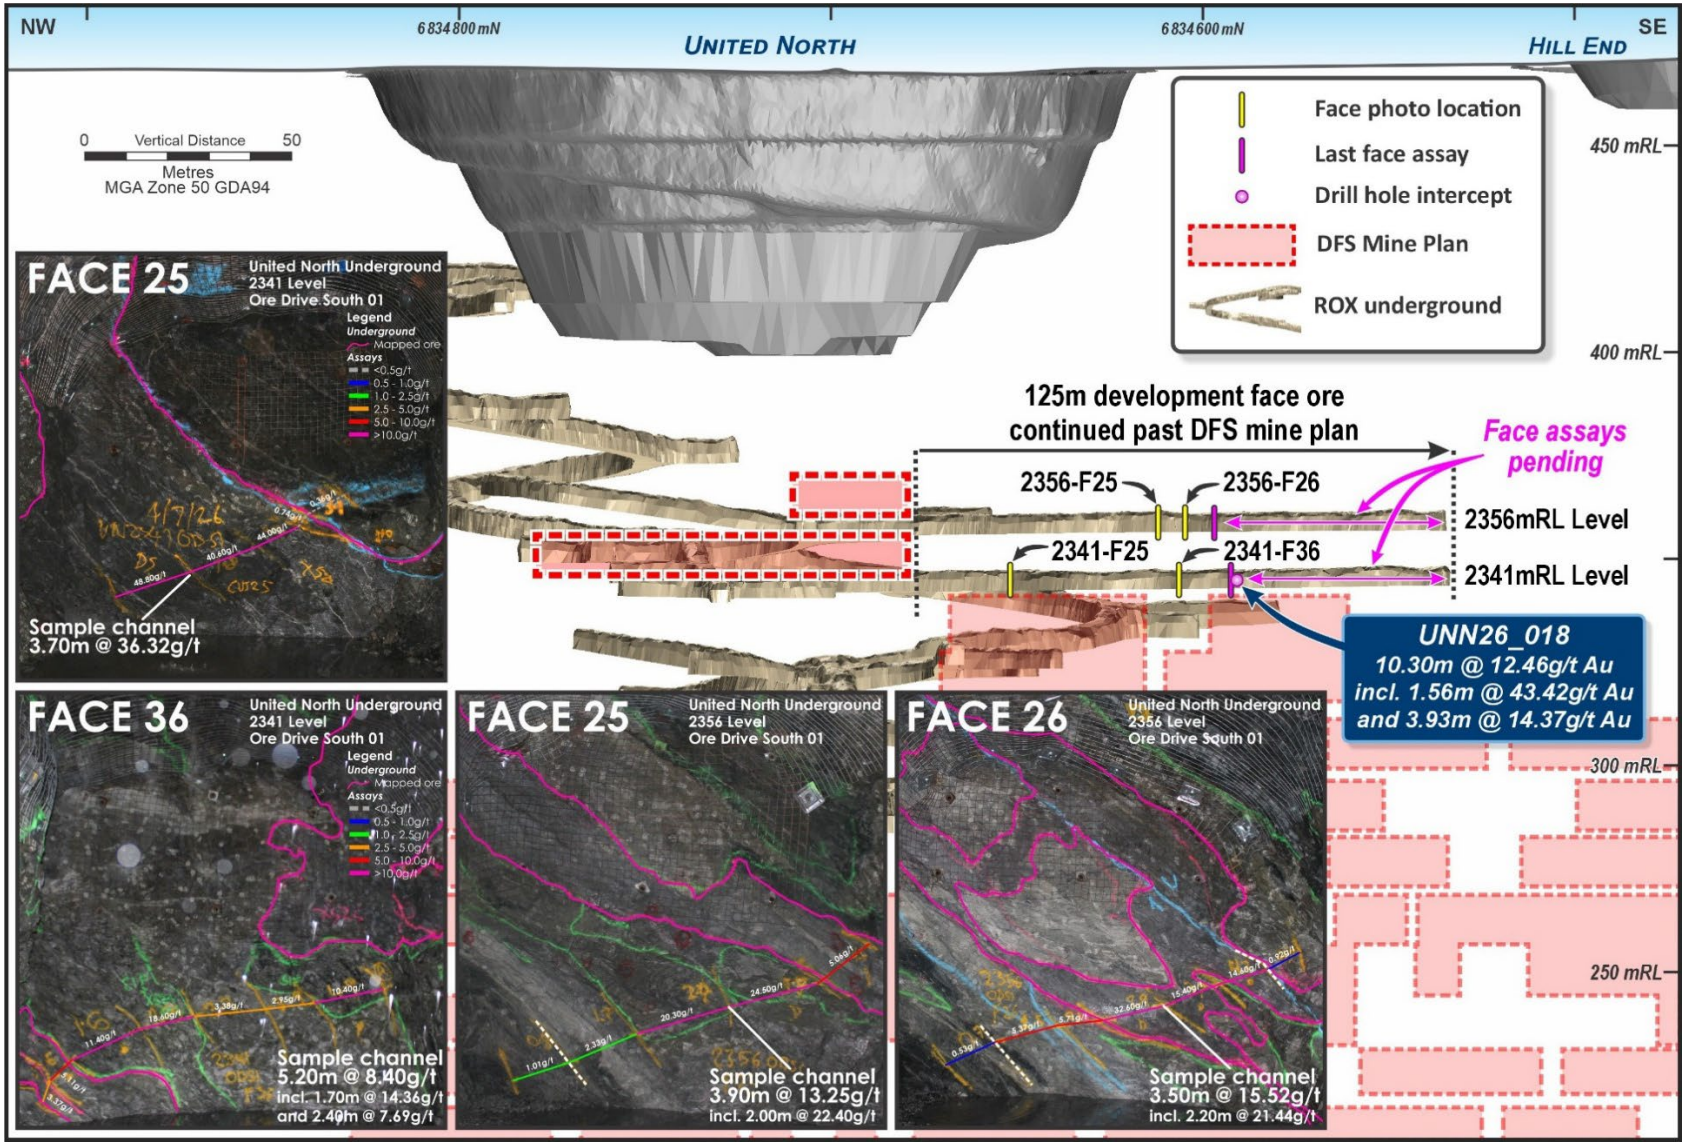


Figure 7 – United North 2356mRL & 2341mRL ore drive development vs. DFS Mine Plan

**Cautionary Note: Channel samples from advancing development on the 2356mRL & 2341mRL levels are operational in nature and are not equivalent to resource definition drilling.*

personal use only

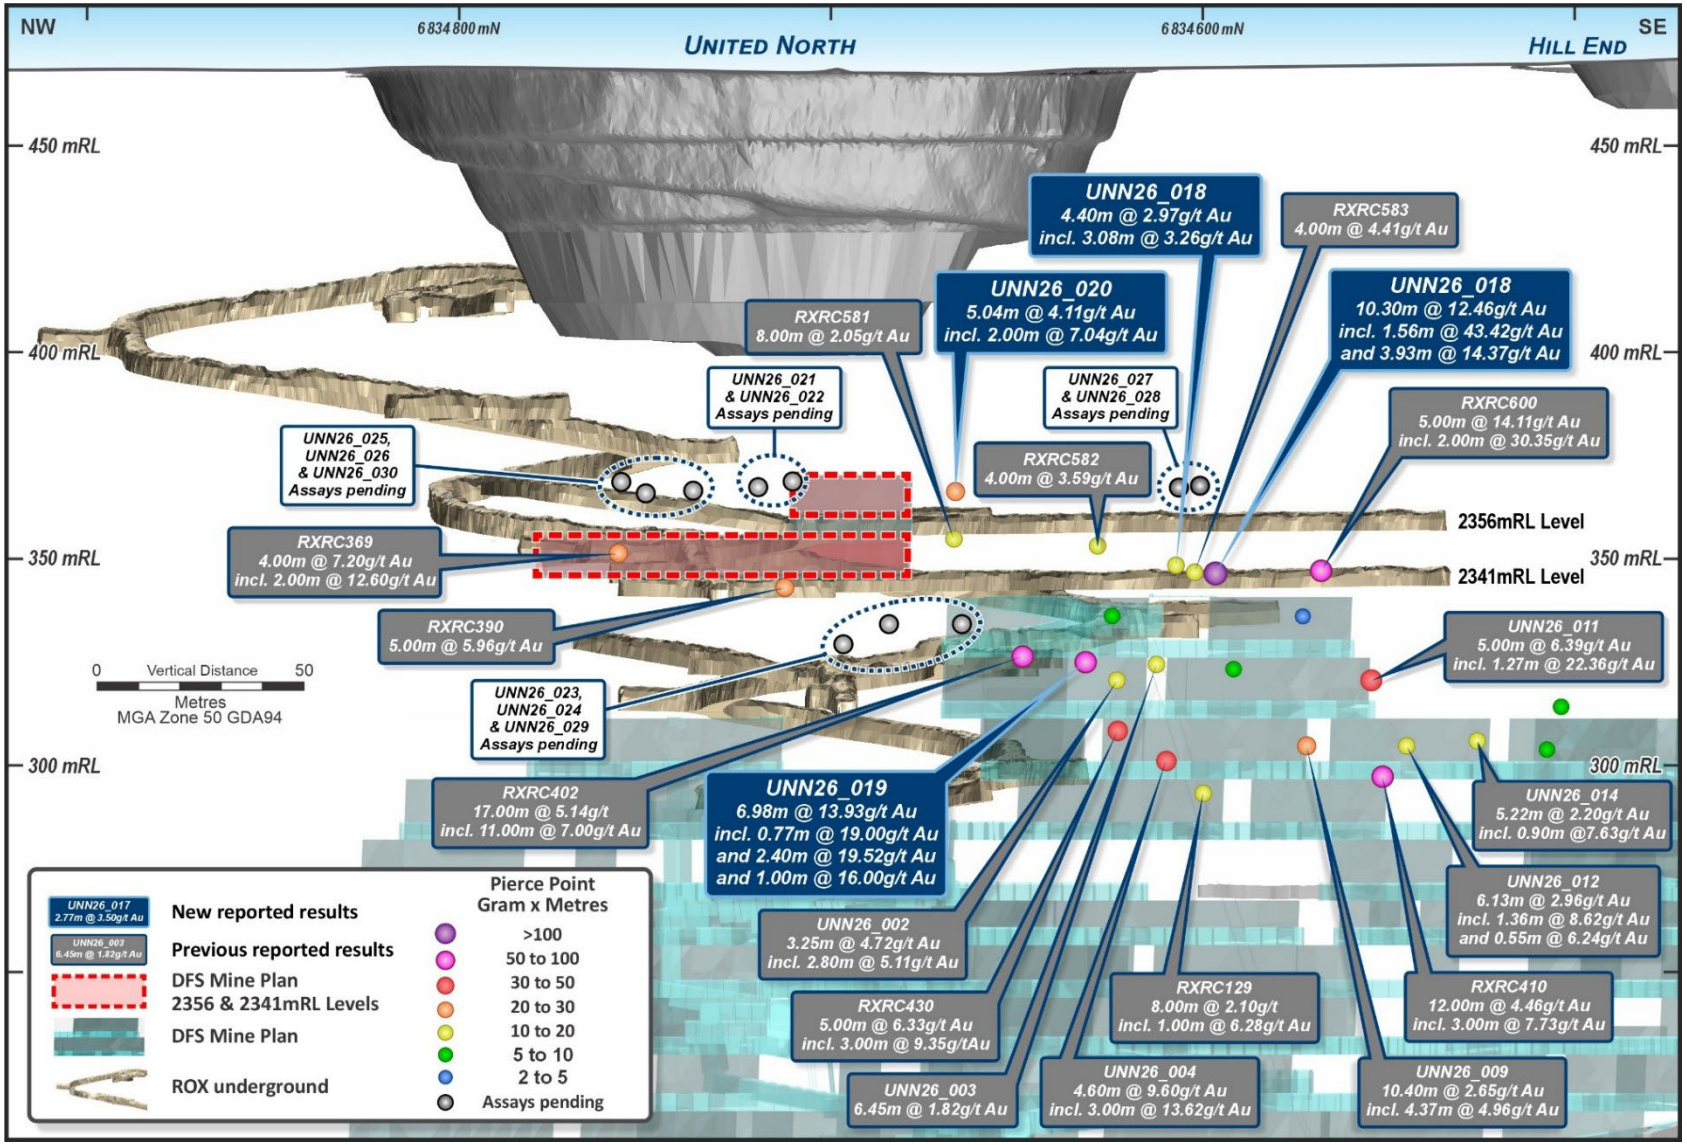


Figure 8 – United North upper levels drilling results

personal use only

Table 3 – United North underground previously reported drilling intercepts shown in Figure 8

Hole ID	Hole Type	From (m)	To (m)	Interval (m)	Au (ppm)	Gram Metres	Date reported
RXRC129	RC	190.00	198.00	8.00	2.10	16.78	20/01/2020
	incl.	194.00	195.00	1.00	6.28	6.28	20/01/2020
RXRC369	RC	131.00	135.00	4.00	7.20	28.80	19/04/2021
	incl.	131.00	133.00	2.00	12.60	25.20	19/04/2021
RXRC390	RC	138.00	143.00	5.00	5.96	29.80	08/07/2021
RXRC402	RC	151.00	168.00	17.00	5.14	87.38	12/08/2021
	incl.	156.00	167.00	11.00	7.00	77.00	12/08/2021
RXRC410	RC	184.00	196.00	12.00	4.46	53.52	09/09/2021
	incl.	186.00	189.00	3.00	7.73	23.19	09/09/2021
RXRC430	RC	180.00	185.00	5.00	6.33	31.65	29/11/2021
	incl.	182.00	185.00	3.00	9.35	28.05	29/11/2021
RXRC581	RC	126.00	134.00	8.00	2.05	16.39	21/04/2026
RXRC582	RC	126.00	130.00	4.00	3.59	14.35	21/04/2026
RXRC583	RC	139.00	143.00	4.00	4.41	17.64	21/04/2026
RXRC600	RC	120.00	125.00	5.00	14.11	70.53	21/04/2026
	incl.	120.00	122.00	2.00	30.35	60.70	21/04/2026
UNN26_002	UGDD	110.55	113.80	3.25	4.72	15.34	17/08/2026
	incl.	111.00	113.80	2.80	5.11	14.32	17/08/2026
UNN26_003	UGDD	105.10	111.55	6.45	1.82	11.73	16/07/2026
UNN26_004	UGDD	131.58	136.18	4.60	9.60	44.18	16/07/2026
	incl.	132.00	135.00	3.00	13.62	40.85	16/07/2026
UNN26_009	UGDD	113.83	124.23	10.40	2.65	27.56	17/08/2026
	incl.	119.86	124.23	4.37	4.96	21.68	17/08/2026
UNN26_011	UGDD	108.00	113.00	5.00	6.39	31.93	17/08/2026
	incl.	110.83	112.10	1.27	22.36	28.39	17/08/2026
UNN26_012	UGDD	118.50	124.63	6.13	2.96	18.16	17/08/2026
	incl.	119.00	120.36	1.36	8.62	11.72	17/08/2026
	and	123.49	124.63	0.55	6.24	3.43	17/08/2026
UNN26_014	UGDD	128.70	133.92	5.22	2.20	11.51	17/08/2026
	incl.	128.70	129.60	0.90	7.63	6.87	17/08/2026
UNN26_014	UGDD	220.70	222.94	2.24	39.33	88.10	17/08/2026

For personal use only

Youanmi Exploration

During the quarter, surface resource definition at the Interceptor prospect, which commenced in the first quarter of CY 2026, was completed. Interceptor, located approximately 100m to the west of and parallel to the Main-Prospect lode trend, returned multiple high-grade intercepts, supporting the mine plan and highlighting potential to extend mineralisation along strike, down dip and plunge.

A structural deformation study was completed alongside regional aeromagnetic interpretation. This work informed the 2026 Mineral Resource Estimate (released 9 September 2026) and provided a framework for identifying multiple structural analogue targets across the Company's tenure.

For the remainder of CY2026, Rox's Youanmi exploration and resource definition drilling programs shifted focus to the Youanmi Deeps targets, with three key objectives:

- Resource conversion: Upgrade Inferred Resources to Indicated Resources (Figure 9).
- Resource growth: Identify additional Inferred Resources (Figure 9), and
- Plunge exploration: Test extensions to known mineralisation (Figure 10)

The diamond drilling program is underway and is expected to continue into early CY2027, alongside ongoing underground drilling operations.

For personal use only

personal use only

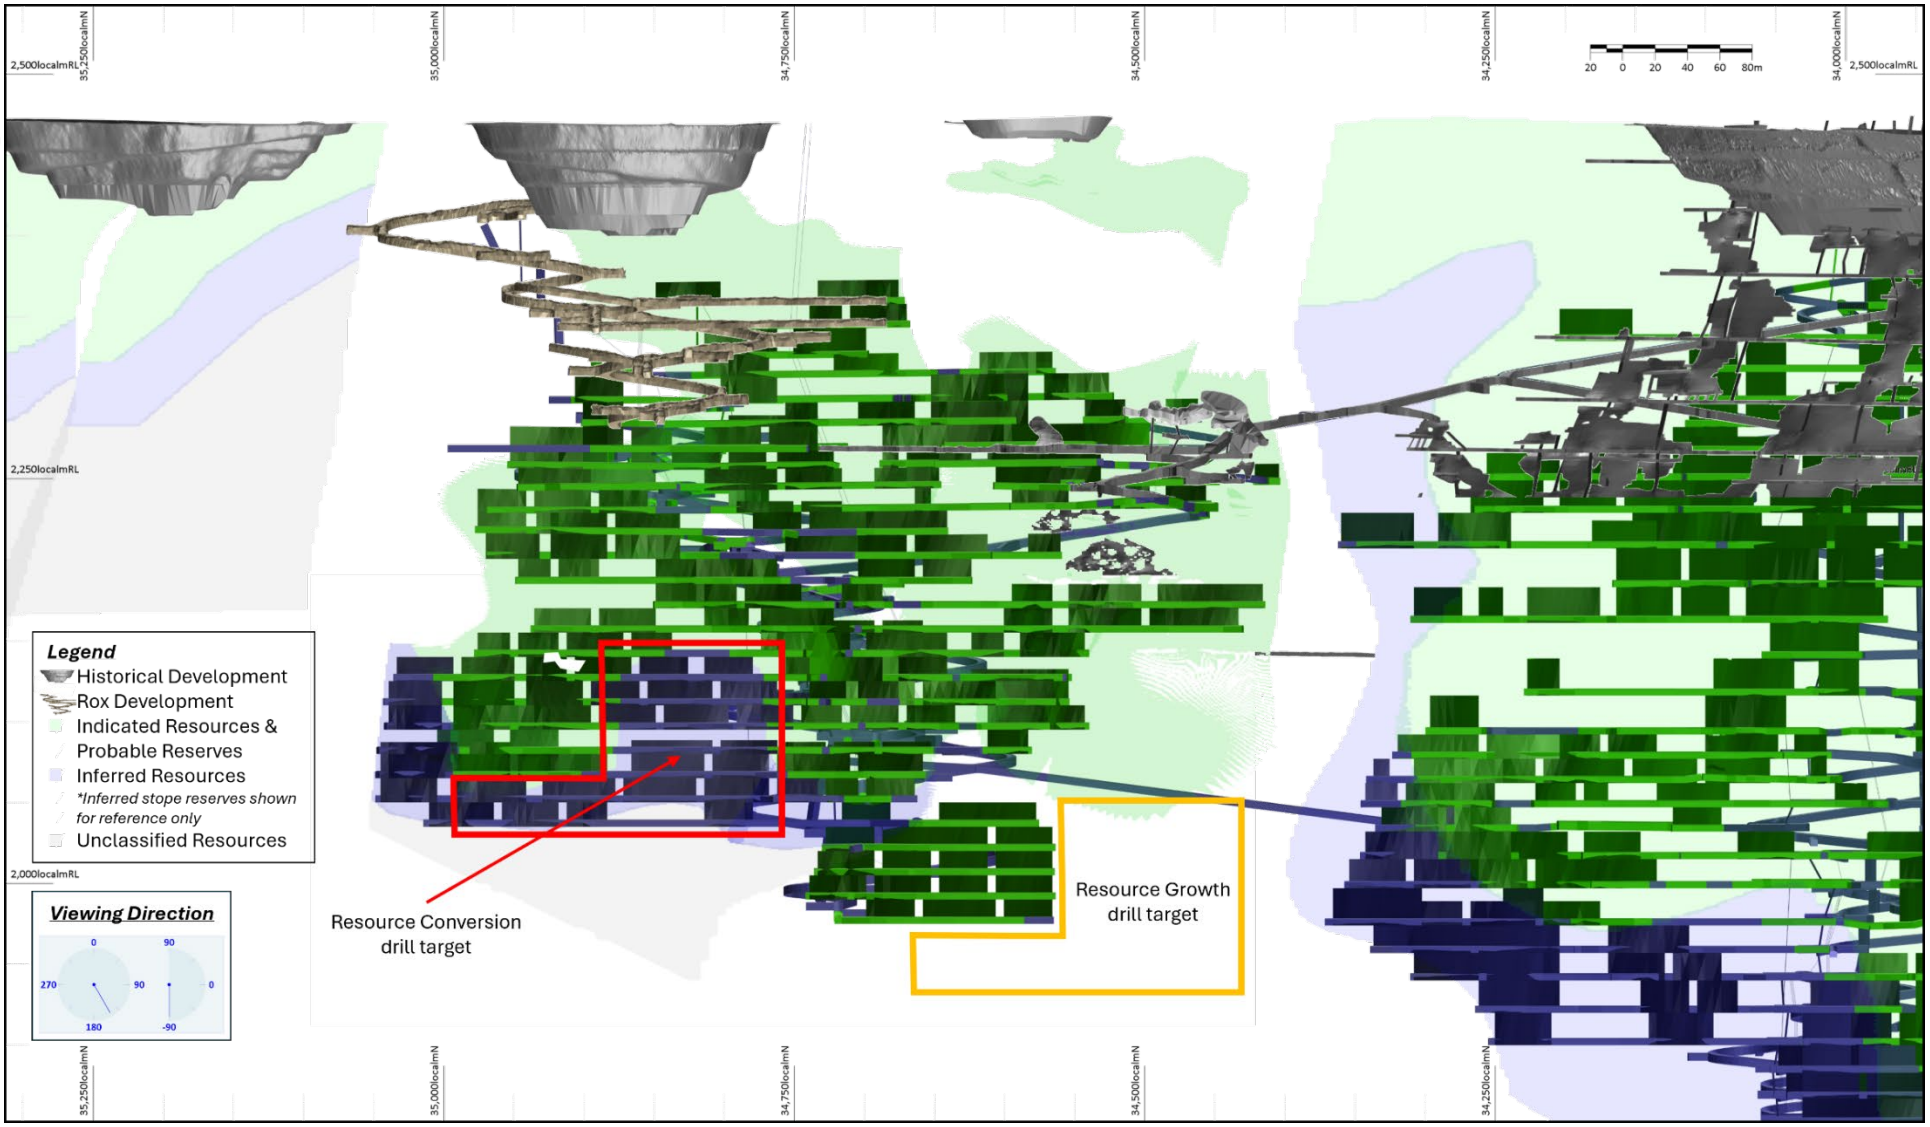


Figure 9 – 2026 Ore Reserves & Mineral Resource Conversion and Resource Growth drilling target areas

personal use only

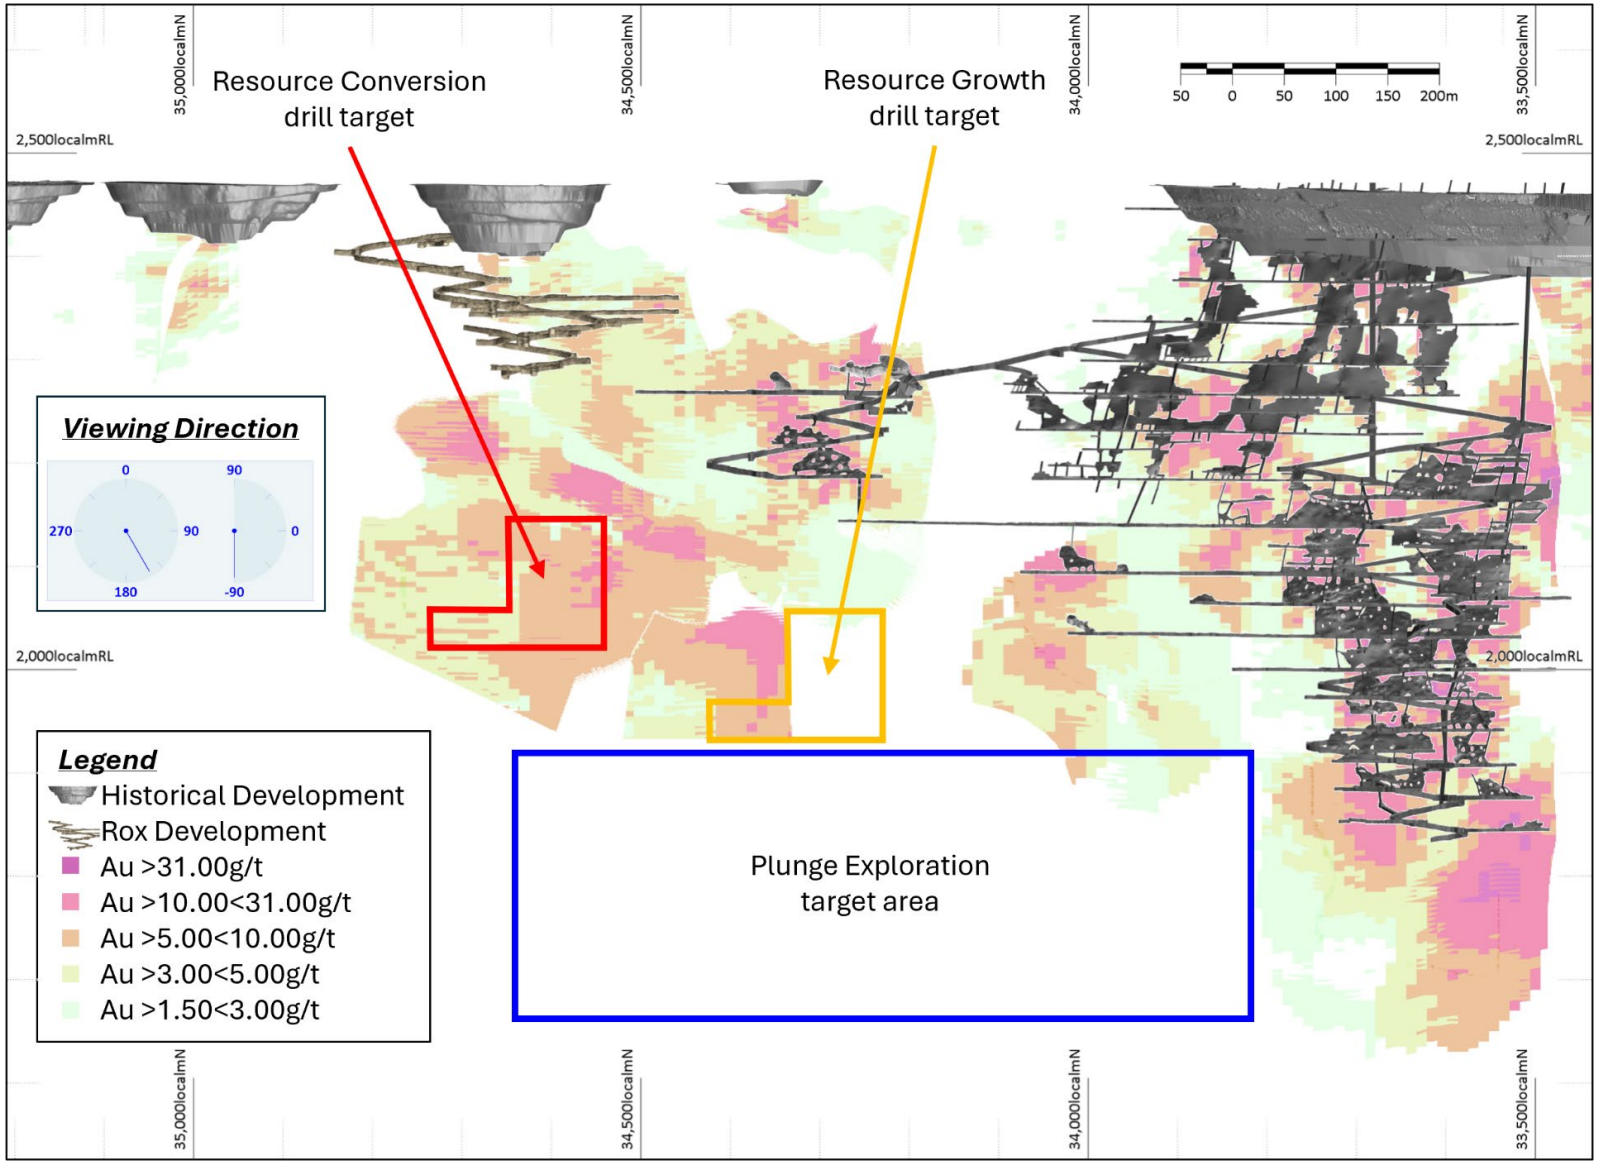


Figure 10 – Plunge Exploration Project area

For personal use only

Hope Exploration

During the quarter, planning and reconnaissance activities commenced to assess the Hope prospect, located approximately 4km northeast of Youanmi Main.

The Hope prospect lies on a granite contact offset along the Youanmi Shear Zone, with structural similarities to the Youanmi mineralisation setting (Figure 11).

Initial aircore drilling is planned to test the geochemical signature of this area, with deeper drilling planned to follow up any favourable assay results.

Regional Exploration

Interpretation of the detailed aeromagnetic survey data acquired and compiled in 2025 was completed during the quarter. Initial analysis identified a previously unexplored target area with structural similarities to the Youanmi mine, located within 20km of the Youanmi processing plant currently under construction (Figure 11).

Reconnaissance and geological mapping planned for the December quarter will help refine these targets ahead of the design of initial drill programs.

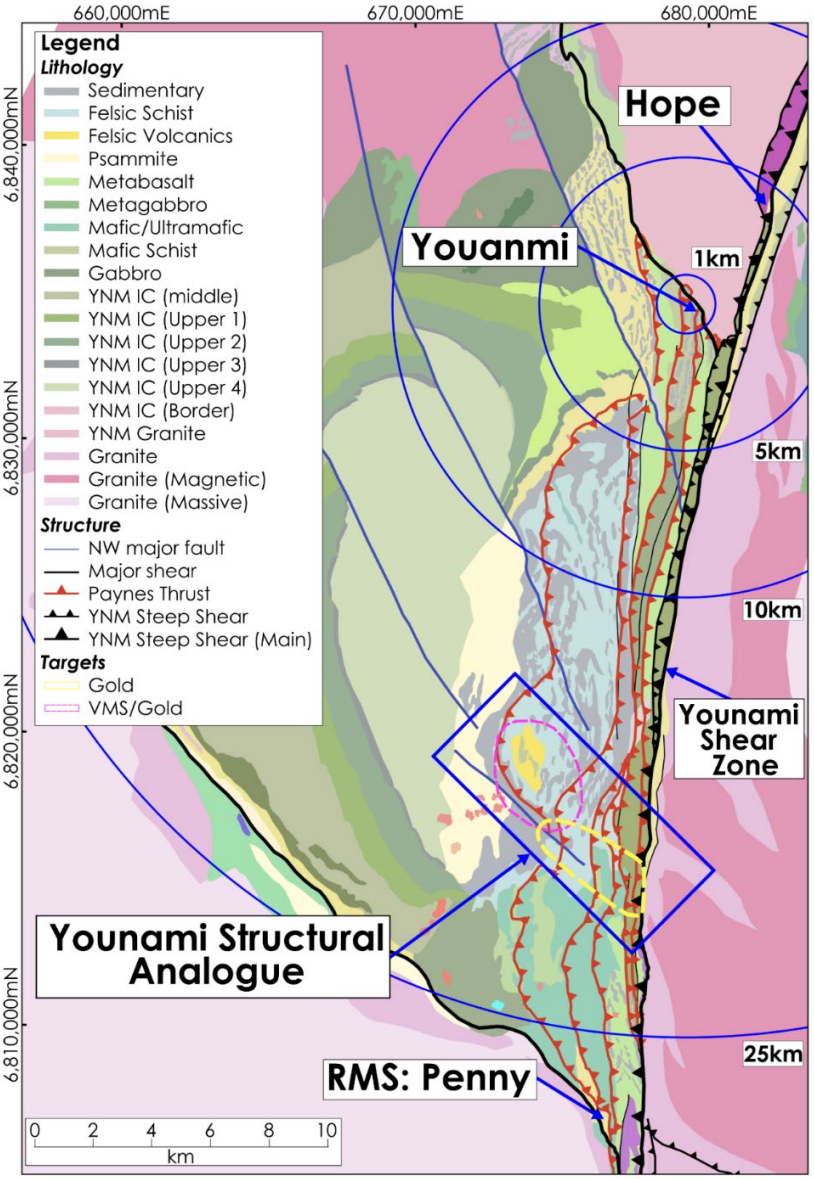


Figure 11 – Simplified aero-magnetic interpreted geology map

For personal use only

Construction of site infrastructure

Works commenced on the supply and installation of the administration and processing office facilities, with completion expected before the end of CY2026.

Construction of the accommodation camp is now complete, following the completion of the fourth and fifth accommodation blocks. Refurbishment of the former dry mess into a new wet mess and social facility has commenced, further enhancing onsite accommodation and amenities (Figure 12).



Figure 12 – Completed camp

During the quarter, a water exploration drilling program was completed to identify potential supplies of 1 litre per second ("L/s") of potable water and up to 13 L/s raw water. The program comprised 17 test bores drilled to varying depths, with potential yields assessed through airlifting, and water quality testing.

Of these 17 test bores, 4 were identified as having strong water supply potential, with production bores and adjacent monitoring bores subsequently installed. Constant-rate pumping tests on these 4 bores are scheduled for the December quarter, with bore field design and cost estimates to follow.

Native Title Agreement

A Native Title Mining Agreement ("Agreement") has been entered into by Rox Resources Limited and its wholly owned subsidiary Rox (Murchison) Pty Ltd with the authorised representatives of the Badimia Barna Native Title Claim Applicant (WAD 258/2024). (see ASX announcement dated 19 August 2026).

The Agreement provides consent from the Badimia Barna Native Title Claim Applicant for the grant and renewal of future project tenements and approvals required for project development, mining and exploration activities across the Company's tenements. It covers Rox's existing project tenure and future tenement applications within the defined project area.

The Agreement also establishes a framework for ongoing cooperation between the parties covering heritage protection, environmental consultation, employment, training and contracting opportunities. The Agreement also includes a package of financial benefits, comprising an upfront payment and a production-based royalty.

For Rox, the Agreement reflects a shared commitment to the responsible development of the Youanmi Gold Mine and establishes a foundation for a constructive, long-term relationship with the Badimia people.

Pathway to Production

Rox's indicative pathway to production remains on track (Figure 13), with key milestones achieved and the following activities underway:

- Definitive Feasibility Study released in November 2025 .
- Project funding secured, including:
    - $200m Placement and $18m Share Purchase Plan completed in December 2025, finalising the equity funding component.
    - $350m Debt Financing facilities secured in March 2026, with Financial Close and first drawdown completed in October 2026.
- Final Investment Decision approved by the Board in March 2026.
- Final environmental approval received in July 2026.
- Dewatering of the Main Pit completed, with dewatering of the historic Youanmi underground workings continuing.
- Mining works underway across all planned declines, with ore stockpiling commenced
- Underground Infill drilling commenced.
- Interquip EPC contract executed, with processing plant construction progressing to plan.

Next steps

- Finalise the oxygen supply agreement, the last remaining major project contract, with a preferred supplier selected and an early works agreement in place.
- Continue advancing near-mine and regional exploration targets.
- Advance underground development across all declines and continue building the ore stockpile ahead of production.

For personal use only

personal use only

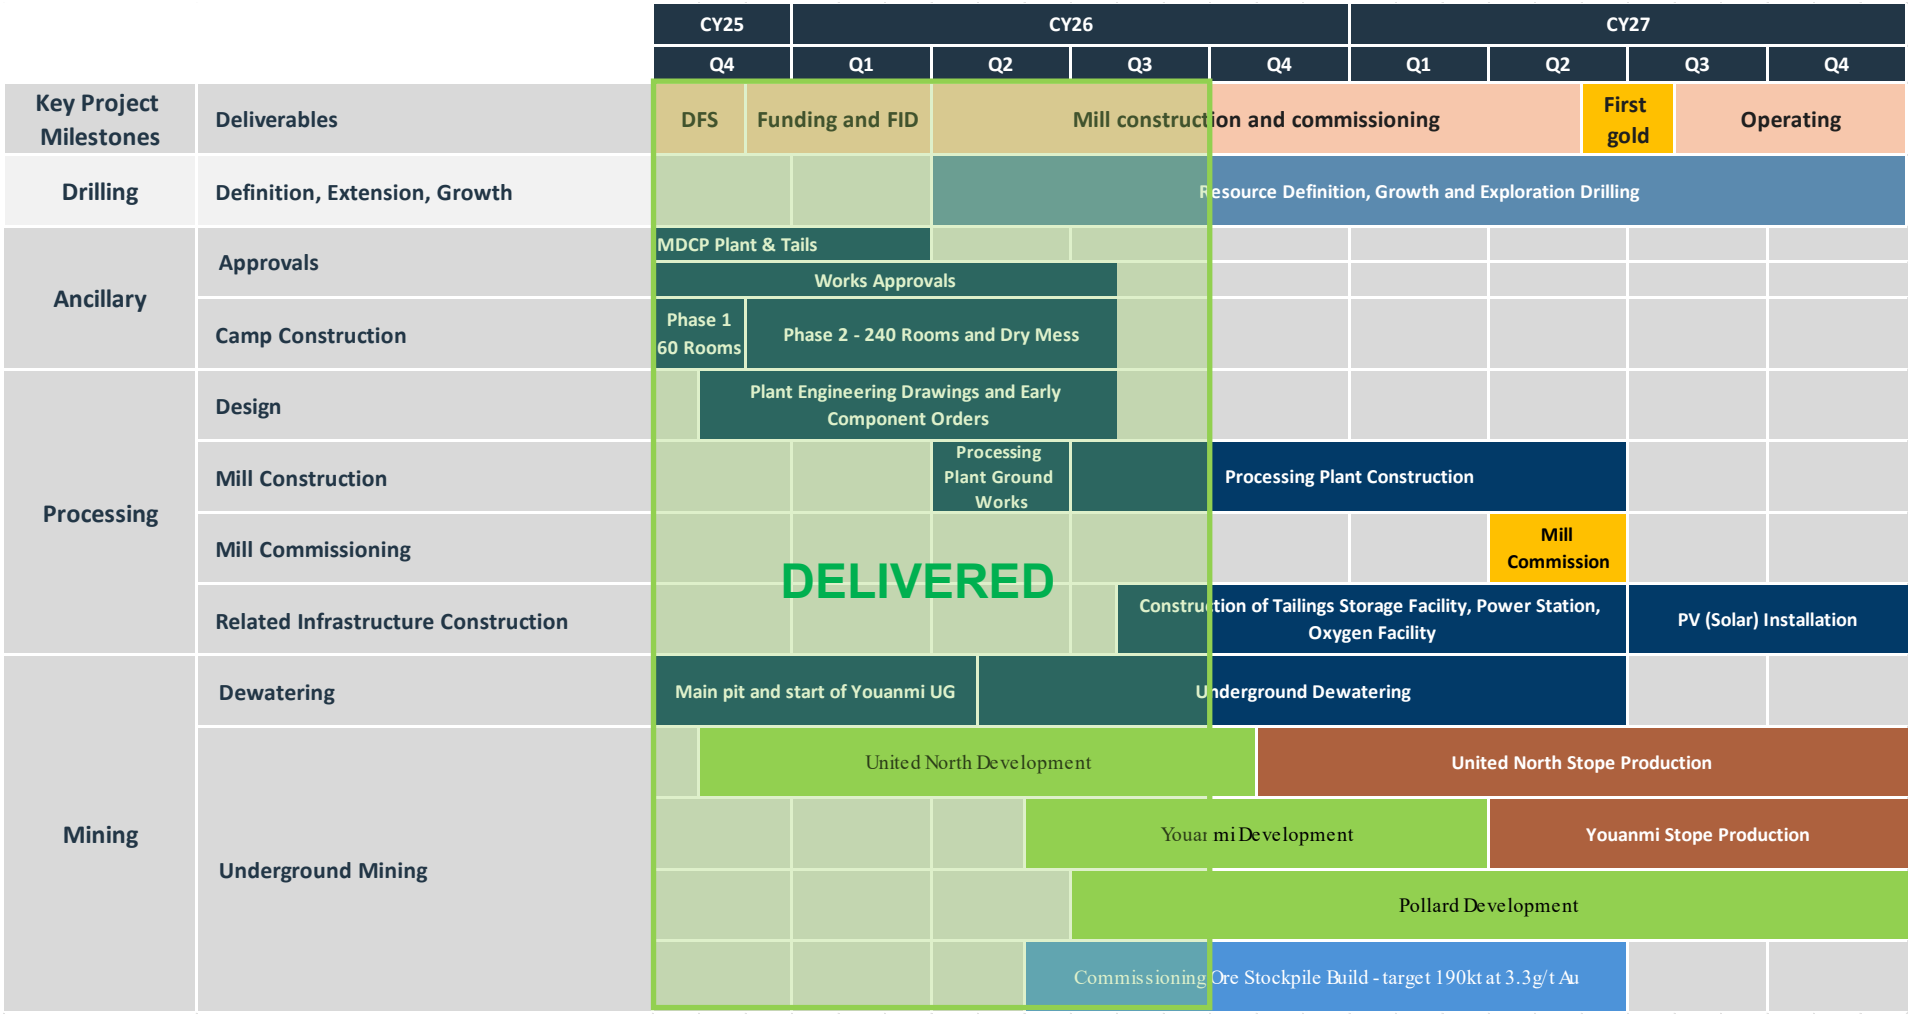


Figure 13 – Indicative Pathway to Production

For personal use only

Corporate

Financial Close and First Drawdown of Debt Facilities

On 2 October 2026, shortly after the end of the Quarter, the Company achieved Financial Close on its $350 million Debt Facilities[4]. The first utilisation of $90.2 million was drawn under the $300 million Senior Secured Project Term Loan Facility, whilst the first utilisation of $4 million was drawn under the Bank Guarantee Facility to support construction and operation of the LNG Facility.

Following the initial utilisation, $229.8 million remains available for drawdown under the Project Debt Facility and the Cost Overrun Facility.

Financials

As at 30 September 2026, the Company's cash balance was $59.3 million, a decrease of $93.4 million from 30 June 2026. The primary cash movements for the quarter were as follows:

Description	$m
Interest & other income	1.8
Exploration and evaluation expenditure	(2.7)
Administration, employee and office expenditure	(2.6)
Mine production expenditure	(3.2)
Mine development expenditure	(19.7)
Acquisition of property plant & equipment	(65.6)
Debt facility transaction costs and lease payments	(1.4)
Total cash movement	**(93.4)**

Payments to related parties of the entity and their associates totalled $412k and consisted of Executive Director remuneration and Non-Executive Director Fees.

Authorisation

This announcement is authorised for release by the Board of Rox Resources Limited.

--- Ends ---

For further information, please contact:

Investor Inquiries
Phillip Wilding
Managing Director & CEO
Rox Resources Limited
admin@roxresources.com.au
+61 8 9226 0044

Media Inquiries
Cara Kennedy
Senior Consultant
SPOKE
cara@hellospoke.com.au
+61 477 771 795

Rox Resources Limited
ABN 53 107 202 602
Level 1, 87 Colin Street, West Perth WA 6005
www.roxresources.com.au

[4] As defined in the ASX Announcement dated 9 March 2026 "Youanmi Fully Funded to Production"

For personal use only

About Rox Resources Limited

Rox Resources (ASX: RXL) is a West Australian focused gold development company. It is the 100% owner of the historic Youanmi Gold Mine near Mt Magnet, approximately 480 kilometres northeast of Perth.

The Company's focus is on the development of the high-grade, high-margin Youanmi Gold Mine that hosts a global mineral resource of 12.4Mt at 5.5g/t for 2.2Moz of gold. With a clear strategic and execution plan to production, Rox Resources offers significant value to its investors.



Corporate Information

Shares on issue	1,393.8 million as at 30 September 2026	
Cash at bank	$59.3 million as at 30 September 2026	
Board	Mr Stephen Dennis (Non-Executive Chairman) Mr Phillip Wilding (Managing Director & CEO) Mr Nathan Stoitis (Non-Executive Director) Mr David Boyd (Non-Executive Director) Mr Alan Rule (Non-Executive Director)	
Major shareholders	L1 Capital Pty Ltd	19.1%
	Hawke's Point Holdings (RRL) L.P.	13.4%
	QGold Pty Ltd	12.1% (related relevant interest)

(As per last lodged substantial holding notices, adjusted for shares issued during the quarter ended 30 September 2026)

Competent Person Statement

Exploration Results

The information in this report that relates to Data and Exploration Results is based on information compiled and reviewed by Jonathan Streeter a Competent Person who is a Fellow Member of the Australian Institute of Geoscientists (AIG), GM Geology at Rox Resources and holds performance rights in the Company. The aforementioned has sufficient experience that is relevant to the style of mineralisation and type of target/deposit under consideration and to the activity which he is undertaking to qualify as a Competent Person as defined in the 2012 Edition of the Australian Code for Reporting of Exploration Results, Mineral Resources and Ore Reserves. Mr Streeter consents to the inclusion in the release of the matters based on the information in the form and context in which it appears.

Where reference is made to previous releases of exploration results in this report, the Company confirms that it is not aware of any new information or data that materially affects the information included in those announcements and all material assumptions and technical parameters underpinning the exploration results included in those announcements continue to apply and have not materially changed.

The information in this report that relates to previous Exploration Results was prepared and first disclosed under the JORC Code 2012 and has been properly and extensively cross-referenced in the text to the date of the original announcement to the ASX.

Resource Statements

The information in this report that relates to Mineral Resources at the Youanmi Gold Project is based on information compiled by Steve Le Brun, a Competent Person who is a Fellow of the Australian Institute of Geoscientists (FAIG) and a Fellow of the Australian Institute of Mining & Metallurgy (FAusIMM). Mr Le Brun is the Principal Resource Geologist for Rox Resources and holds shares and performance rights in the Company. Mr Le Brun has sufficient experience that is relevant to the style of mineralisation and type of deposit under consideration and to the activity being undertaken to qualify as a Competent Person as defined in the 2012 Edition of the 'Australasian Code for Reporting of Exploration Results, Mineral Resources and Ore Reserves'. Mr Le Brun consents to the inclusion in this report of the matters based on his information in the form and context in which it appears.

Ore Reserves

The information in this announcement that relates to Ore Reserves is based on information compiled by Daniel Marchesi, a Competent Person who is a Member of the Australasian Institute of Mining and Metallurgy and a full-time employee of Rox Resources Limited. Mr Marchesi has sufficient experience which is relevant to the style of mineralisation and type of deposit under consideration and to the activity being undertaken to qualify as a Competent Person as defined in the 2012 Edition of the 'Australasian Code for Reporting of Exploration Results, Mineral Resources and Ore Reserves'. Mr Marchesi consents to the inclusion in this announcement of the matters based on this information in the form and context in which it appears

Forward-Looking Statements

Certain statements in this announcement relate to the future, including forward-looking statements relating to the Company and its business (including its projects). Forward-looking statements include, but are not limited to, statements concerning Rox Resources Limited planned exploration program(s) and other statements that are not historical facts. When used in this document, the words such as "could," "plan," "estimate," "expect," "intend," "may", "potential," "should," and similar expressions are forward looking statements.

These forward-looking statements involve known and unknown risks, uncertainties, assumptions, and other important factors that could cause the actual results, performance or achievements of the Company to be materially different from future results, performance or achievements expressed or implied by such statements. Actual events or results may differ materially from the events or results expressed or implied in any forward-looking statement and deviations are both normal and to be expected. Neither the Company, its officers nor any other person gives any representation, assurance or guarantee that the events or other matters expressed or implied in any forward-looking statements will actually occur. You are cautioned not to place undue reliance on those statements.

For personal use only

For personal use only

Appendix 1

Schedule of Mining Tenements 30 September 2026

Project	Tenement Number	Interest	Interest held
Youanmi Gold Project, WA	E57/1121	All Minerals	100%
	E57/1122	All Minerals	100%
	E57/1123	All Minerals	100%
	E57/1236	All Minerals	100%
	E57/1237	All Minerals	100%
	E57/1387	All Minerals	100%
	E57/1425	Application	0%
	E57/1477	All Minerals	100%
	E57/1492	Application	0%
	E57/1493	Application	0%
	E57/1500	Application	0%
	L57/0058	Airstrip	100%
	L57/0059	Infrastructure	100%
	M57/0010	All Minerals	100%
	M57/0051	All Minerals	100%
	M57/0075	All Minerals	100%
	M57/0097	All Minerals	100%
	M57/0109	All Minerals	100%
	M57/0135	All Minerals	100%
	M57/0160A	All Minerals	100%
	M57/0164	All Minerals	100%
	M57/0165	All Minerals	100%
	M57/0166	All Minerals	100%
	M57/0167	All Minerals	100%
Youanmi - Sandstone Youanmi JV	E57/0985	Gold Rights	90%
	E57/0986	Gold Rights	90%
	E57/1011-1	Gold Rights	90%
Youanmi, WA	E57/0982	Gold Rights	100%
	E57/1018	Gold Rights	100%
	E57/1019	Gold Rights	100%
	E57/1023-I	Gold Rights	100%
	E57/1078	Gold Rights	100%
Youanmi - Currans JV, WA [1]	M57/0641	Gold Rights[1]	90%[1]
	M57/0642	Gold Rights[1]	90%[1]

Notes:

1. 90% interest in Gold Rights and 45% interest in all other minerals
2. No tenements were acquired or disposed of in the quarter

Appendix 5B

Mining exploration entity or oil and gas exploration entity quarterly cash flow report

Name of entity

Rox Resources Limited

ABN	Quarter ended ("current quarter")
53 107 202 602	**30 September 2026**

Consolidated statement of cash flows		**Current quarter $A'000**	**Year to date (3 months) $A'000**
1.	**Cash flows from operating activities**		
1.1	Receipts from customers	-	-
1.2	Payments for		
	(a) exploration & evaluation	(2,684)	(2,684)
	(b) development	-	-
	(c) production	(3,224)	(3,224)
	(d) staff costs	(542)	(542)
	(e) administration and corporate costs	(2,030)	(2,030)
1.3	Dividends received (see note 3)	-	-
1.4	Interest received	1,817	1,817
1.5	Interest and other costs of finance paid	-	-
1.6	Income taxes paid	-	-
1.7	Government grants and tax incentives	-	-
1.8	Other (provide details if material)	-	-
1.9	**Net cash from / (used in) operating activities**	**(6,663)**	**(6,663)**

2.	**Cash flows from investing activities**		
2.1	Payments to acquire or for:		
	(a) entities	-	-
	(b) tenements	-	-
	(c) property, plant and equipment	(65,587)	(65,587)
	(d) exploration & evaluation	-	-
	(e) investments	-	-
	(f) other (mine development - assets under construction)	(19,673)	(19,673)

For personal use only

For personal use only

Consolidated statement of cash flows		Current quarter $A'000	Year to date (3 months) $A'000
2.2	Proceeds from the disposal of:		
	(a) entities	-	-
	(b) tenements	-	-
	(c) property, plant and equipment	-	-
	(d) investments	-	-
	(e) other non-current assets	-	-
2.3	Cash flows from loans to other entities	-	-
2.4	Dividends received (see note 3)	-	-
2.5	Other (provide details if material)	-	-
2.6	**Net cash from / (used in) investing activities**	**(85,260)**	**(85,260)**

3.	**Cash flows from financing activities**		
3.1	Proceeds from issues of equity securities (excluding convertible debt securities)	-	-
3.2	Proceeds from issue of convertible debt securities	-	-
3.3	Proceeds from exercise of options	-	-
3.4	Transaction costs related to issues of equity securities or convertible debt securities	-	-
3.5	Proceeds from borrowings	-	-
3.6	Repayment of borrowings	-	-
3.7	Transaction costs related to loans and borrowings	(1,402)	(1,402)
3.8	Dividends paid	-	-
3.9	Other (repayment of office lease liability)	(81)	(81)
3.10	**Net cash from / (used in) financing activities**	**(1,483)**	**(1,483)**

4.	**Net increase / (decrease) in cash and cash equivalents for the period**		
4.1	Cash and cash equivalents at beginning of period	152,666	152,666
4.2	Net cash from / (used in) operating activities (item 1.9 above)	(6,663)	(6,663)
4.3	Net cash from / (used in) investing activities (item 2.6 above)	(85,260)	(85,260)
4.4	Net cash from / (used in) financing activities (item 3.10 above)	(1,483)	(1,483)

Consolidated statement of cash flows		Current quarter $A'000	Year to date (3 months) $A'000
4.5	Effect of movement in exchange rates on cash held	-	-
4.6	**Cash and cash equivalents at end of period**	**59,260**	**59,260**

5.	Reconciliation of cash and cash equivalents at the end of the quarter (as shown in the consolidated statement of cash flows) to the related items in the accounts	Current quarter $A'000	Previous quarter $A'000
5.1	Bank balances	58,936	112,342
5.2	Call deposits	324	40,324
5.3	Bank overdrafts	-	-
5.4	Other (provide details)	-	-
5.5	**Cash and cash equivalents at end of quarter (should equal item 4.6 above)**	**59,260**	**152,666**

6.	Payments to related parties of the entity and their associates	Current quarter $A'000
6.1	Aggregate amount of payments to related parties and their associates included in item 1	412
6.2	Aggregate amount of payments to related parties and their associates included in item 2	-

Note: if any amounts are shown in items 6.1 or 6.2, your quarterly activity report must include a description of, and an explanation for, such payments.

For personal use only

For personal use only

7.	**Financing facilities** *Note: the term "facility' includes all forms of financing arrangements available to the entity.* *Add notes as necessary for an understanding of the sources of finance available to the entity.*	**Total facility amount at quarter end $A'000**	**Amount drawn at quarter end $A'000**
7.1	Loan facilities	320,000	-
7.2	Credit standby arrangements	-	-
7.3	Other (Bank Guarantee Facility)	30,000	-
7.4	**Total financing facilities**	**350,000**	-

7.5	**Unused financing facilities available at quarter end**	**350,000**

7.6 Include in the box below a description of each facility above, including the lender, interest rate, maturity date and whether it is secured or unsecured. If any additional financing facilities have been entered into or are proposed to be entered into after quarter end, include a note providing details of those facilities as well.

The Debt Facilities, announced on 7 April 2026, comprise a $300 million Senior Secured Project Term Loan Facility, a $20 million Cost Overrun Facility and a $30 million Bank Guarantee Facility, provided by a syndicate of lenders under the Syndicated Facility Agreement.

During the quarter ended 30 September 2026, the Company satisfied all conditions precedent to the initial drawdown of the Debt Facilities.

Subsequent to the end of the quarter, on 2 October 2026, the Company made its first drawdown of the Debt Facilities of $90.2 million under the Project Term Loan Facility and utilised $4 million under the Bank Guarantee Facility. (see ASX announcement "*Financial Close and First Drawdown*" on 5 October 2026)

8.	**Estimated cash available for future operating activities**	**$A'000**
8.1	Net cash from / (used in) operating activities (item 1.9)	(6,663)
8.2	(Payments for exploration & evaluation classified as investing activities) (item 2.1(d))	-
8.3	Total relevant outgoings (item 8.1 + item 8.2)	(6,663)
8.4	Cash and cash equivalents at quarter end (item 4.6)	59,260
8.5	Unused finance facilities available at quarter end (item 7.5)	350,000
8.6	Total available funding (item 8.4 + item 8.5)	409,260
8.7	**Estimated quarters of funding available (item 8.6 divided by item 8.3)**	**61.42**

Note: if the entity has reported positive relevant outgoings (ie a net cash inflow) in item 8.3, answer item 8.7 as "N/A". Otherwise, a figure for the estimated quarters of funding available must be included in item 8.7.

8.8 If item 8.7 is less than 2 quarters, please provide answers to the following questions:

8.8.1 Does the entity expect that it will continue to have the current level of net operating cash flows for the time being and, if not, why not?

Answer: Not applicable

8.8.2 Has the entity taken any steps, or does it propose to take any steps, to raise further cash to fund its operations and, if so, what are those steps and how likely does it believe that they will be successful?

Answer: Not applicable

8.8.3	Does the entity expect to be able to continue its operations and to meet its business objectives and, if so, on what basis?
Answer: Not applicable	
Note: where item 8.7 is less than 2 quarters, all of questions 8.8.1, 8.8.2 and 8.8.3 above must be answered.	

Compliance statement

1 This statement has been prepared in accordance with accounting standards and policies which comply with Listing Rule 19.11A.

2 This statement gives a true and fair view of the matters disclosed.

Date: 20 October 2026

Authorised by: The Board of Directors

Notes

1. This quarterly cash flow report and the accompanying activity report provide a basis for informing the market about the entity's activities for the past quarter, how they have been financed and the effect this has had on its cash position. An entity that wishes to disclose additional information over and above the minimum required under the Listing Rules is encouraged to do so.
2. If this quarterly cash flow report has been prepared in accordance with Australian Accounting Standards, the definitions in, and provisions of, *AASB 6: Exploration for and Evaluation of Mineral Resources* and *AASB 107: Statement of Cash Flows* apply to this report. If this quarterly cash flow report has been prepared in accordance with other accounting standards agreed by ASX pursuant to Listing Rule 19.11A, the corresponding equivalent standards apply to this report.
3. Dividends received may be classified either as cash flows from operating activities or cash flows from investing activities, depending on the accounting policy of the entity.
4. If this report has been authorised for release to the market by your board of directors, you can insert here: "By the board". If it has been authorised for release to the market by a committee of your board of directors, you can insert here: "By the [*name of board committee – eg Audit and Risk Committee*]". If it has been authorised for release to the market by a disclosure committee, you can insert here: "By the Disclosure Committee".
5. If this report has been authorised for release to the market by your board of directors and you wish to hold yourself out as complying with recommendation 4.2 of the ASX Corporate Governance Council's *Corporate Governance Principles and Recommendations*, the board should have received a declaration from its CEO and CFO that, in their opinion, the financial records of the entity have been properly maintained, that this report complies with the appropriate accounting standards and gives a true and fair view of the cash flows of the entity, and that their opinion has been formed on the basis of a sound system of risk management and internal control which is operating effectively.

For personal use only
